DOST ScINET-PHIL
http://scinet.dost.gov.ph

DOST-STII
Department of Science and Technology
SCIENCE AND TECHNOLOGY INFORMATION INSTITUTE

LitPath AI: Smart Pathfinder for Theses and Dissertations

Group HecTech

Project Management

PROJMAN MI231

Mr. Jose Eugenio L. Quesada

DOST ScINET-PHIL
http://scinet.dost.gov.ph

DOST-STII
Department of Science and Technology
SCIENCE AND TECHNOLOGY INFORMATION INSTITUTE

OUR TEAM

Mr. Gonzalo V. Gumogda
Project Adviser

Cempron, Charijoy

Sta Ana, Joshua

Dulay, Jenine Elaine

Tomon, Tracie

Table of Contents

1 Agile Scrum Ceremonies
2 Agile Scrum Documents
3 PMBOK: Initiation Phase
4 PMBOK: Planning Phase
5 Costs
6 System Design Document
7 OpenProject

AGILE SCRUM CEREMONIES

DOST ScINET-PHIL
http://scinet.dost.gov.ph

Agile Scrum Ceremonies

Sprint Planning

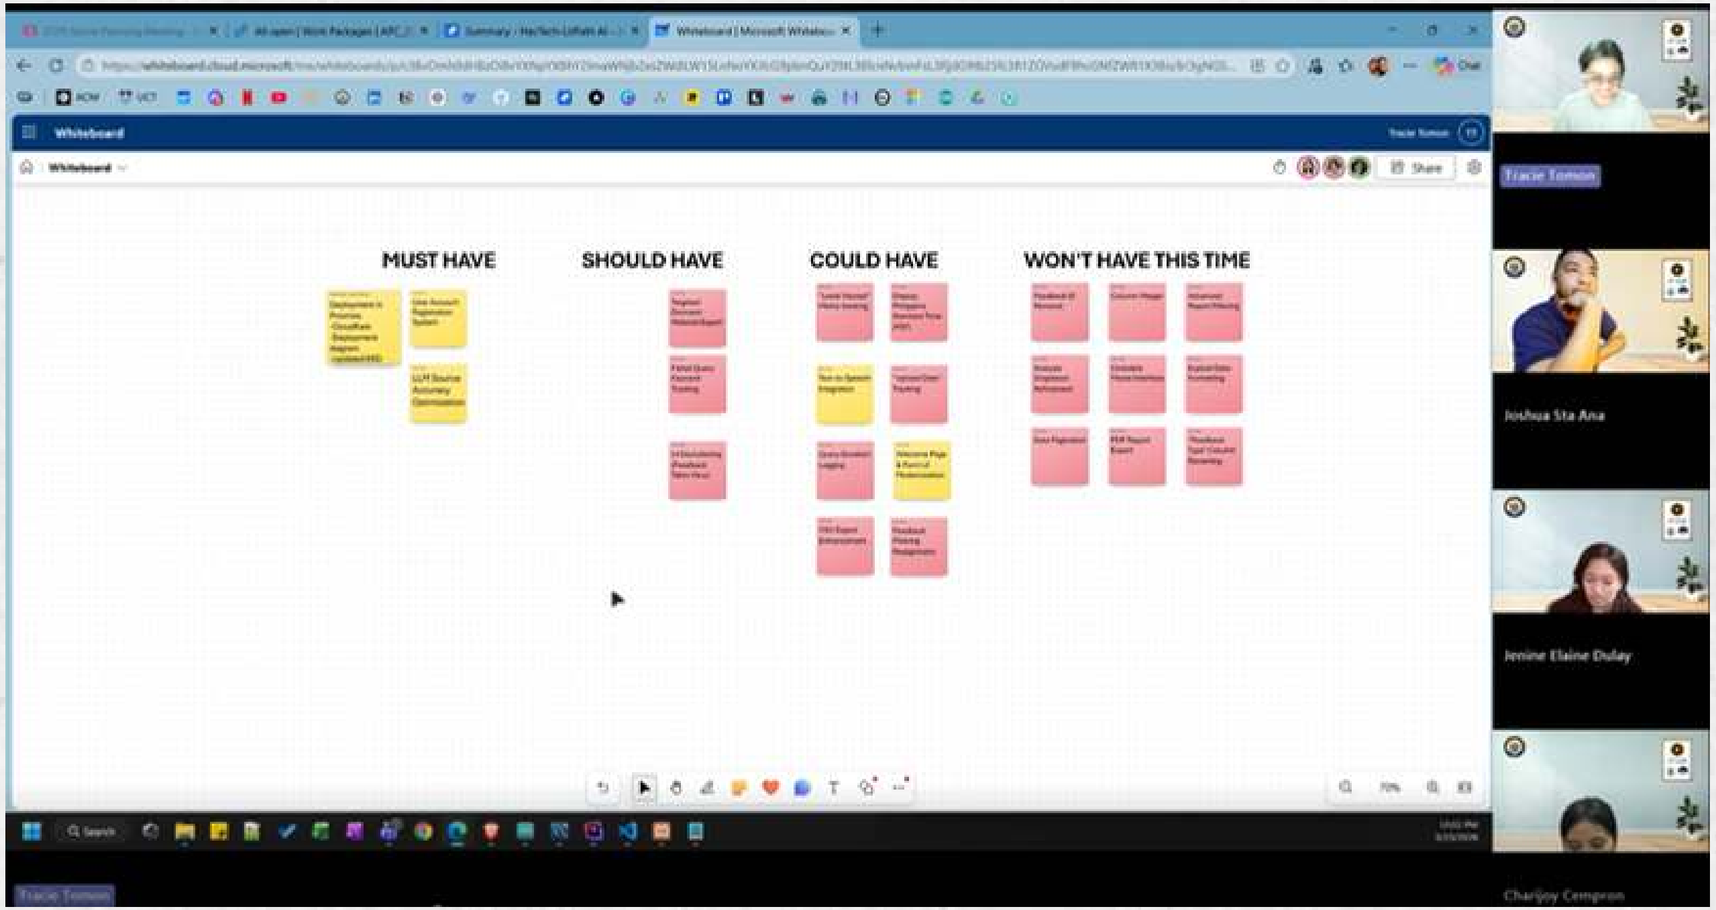

Tomon, Tracie

DOST ScINET-PHIL
http://scinet.dost.gov.ph

Agile Scrum Ceremonies

Daily Stand-Up

APC_2025_2026_T1_MI231_G0... / Forums / AY 2025-2026 T3 Sprint 01 Dai... / Sprint 1 Week 1 Day 01 Daily ...

Sprint 1 Week 1 Day 01 Daily Scrum Meeting Individual Updated Report (March 25, 2026)

Added by Tracie Tomon 21 days ago

Answer the following questions:

1. What did you accomplish yesterday?
2. What can I commit today?
3. Anything blocking my progress?

Replies (4)

JD *RE: Sprint 1 Week 1 Day 01 Daily Scrum Meeting Individual Updated Report (March 25, 2026)* - **Added by** *Jenine Elaine Dulay 21 days* **ago**

1. **What did you accomplish yesterday?**
   - Updated the background blur effect on the welcome page.
2. **What can I commit today?**
   - Start on the "UI decluttering" work package.
3. **Anything blocking my progress?**
   - Limited availability due to house chores and other subject-related assignments.

TT *RE: Sprint 1 Week 1 Day 01 Daily Scrum Meeting Individual Updated Report (March 25, 2026)* - **Added by** *Tracie Tomon 20 days* **ago**

1. What did you accomplish yesterday?
   - Set up Forum for the Daily Scrum reports. Reviewed some of the PMBOK 40 processes.
2. What can I commit today?
   - Prepare the agenda for tomorrow's consultation meeting with the advisers. Set up the schedules for the two meetings.
3. Anything blocking my progress?
   - Work schedule

CC *RE: Sprint 1 Week 1 Day 01 Daily Scrum Meeting Individual Updated Report (March 25, 2026)* - **Added by** *Charijoy Cempron 20 days* **ago**

1. What did you accomplish yesterday?
   - Created minutes of the meeting.
2. What can I commit today?
   - Create minutes of the meeting and start the registration feature.
3. Anything blocking my progress?
   - Other subjects.

JA *RE: RE: Sprint 1 Week 1 Day 01 Daily Scrum Meeting Individual Updated Report (March 25, 2026)* - **Added by** *Joshua Sta Ana 18 days* **ago**

1. What did you accomplish yesterday?
   - Planned and started building an on-prem server for github clonning and environment setup
2. What can I commit today?
   - Contininuing review of project documentations, recordings and work packages to update
   - Research for more deployment tools/platforms, Dev/Ops solutions.
3. Anything Blocking my progress?
   - Personal and work schedules/ agendas.

APC_2025_2026_T1_MI231_G0... / Forums / AY 2025-2026 T3 Sprint 01 Dai... / Sprint 1 Week 2 Day 03 Daily ...

Sprint 1 Week 2 Day 03 Daily Scrum Meeting Individual Updated Report (April 1, 2026)

Added by Tracie Tomon 15 days ago

Answer the following questions:

1. What did you accomplish yesterday?
2. What can I commit today?
3. Anything blocking my progress?

Replies (4)

TT *RE: Sprint 1 Week 2 Day 03 Daily Scrum Meeting Individual Updated Report (April 1, 2026)* - **Added by** *Tracie Tomon 14 days* **ago**

1. What did you accomplish yesterday?
   - Started coding the Failed Query content for the admin dashboard and reviewed the 02 Planning documents to finalize the designations.
2. What can I commit today?
   - Continue working on system development and documentation, as well as updating the work packages.
3. Anything blocking my progress?
   - Holy Week schedule and work schedule.

CC *RE: Sprint 1 Week 2 Day 03 Daily Scrum Meeting Individual Updated Report (April 1, 2026)* - **Added by** *Charijoy Cempron 13 days* **ago**

1. What did you accomplish yesterday?
   - I found the stakeholder analysis file from MSYADD and updated OpenProject details except for budget and cost.
2. What can I commit today?
   - I will do the planning phase documents assigned to me and to help in the initiation phase document group work.
3. Anything blocking my progress?
   - Other subjects.

JD *RE: Sprint 1 Week 2 Day 03 Daily Scrum Meeting Individual Updated Report (April 1, 2026)* - **Added by** *Jenine Elaine Dulay 10 days* **ago**

1. **What did you accomplish yesterday?**
   - Yesterday, I started the Business Case Document.
2. **What can I commit today?**
   - I will continue to work on the Business Case Document.
3. **Anything blocking my progress?**
   - Holy week plans and other subject-related assignments.

JA *RE: RE: Sprint 1 Week 2 Day 03 Daily Scrum Meeting Individual Updated Report (April 1, 2026)* - **Added by** *Joshua Sta Ana 10 days* **ago**

- **What did you accomplish yesterday?**
  OPEN PROJECT - *rasci matrix/ features to log user stories and task budget costing -Created a separate draft or completion and posting to Open project*
  PMBOK requirements - *started the 01 Initation documentaion specific to Project brief template and statement of work draft for checking*
  DEPLOYMENT -*Proxmox server already installed, configured for remote access.*
- **What can I commit today?**
  Will start the project feature development in VSCODE

  01 Initation documentaion requirements continuation, assigned and group work
  -Project brief template
  -Statement of work

  Will start Ubuntu server instance creation to proxmox and configuration
  -Github clonning
  -CI/CD workflows to Github and Vscode
- **Anything blocking my progress?**
  Holy week plans, limited iternet bandwidth

Tomon, Tracie

DOST ScINET-PHIL
http://scinet.dost.gov.ph

Agile Scrum Ceremonies

Product Backlog Refinement

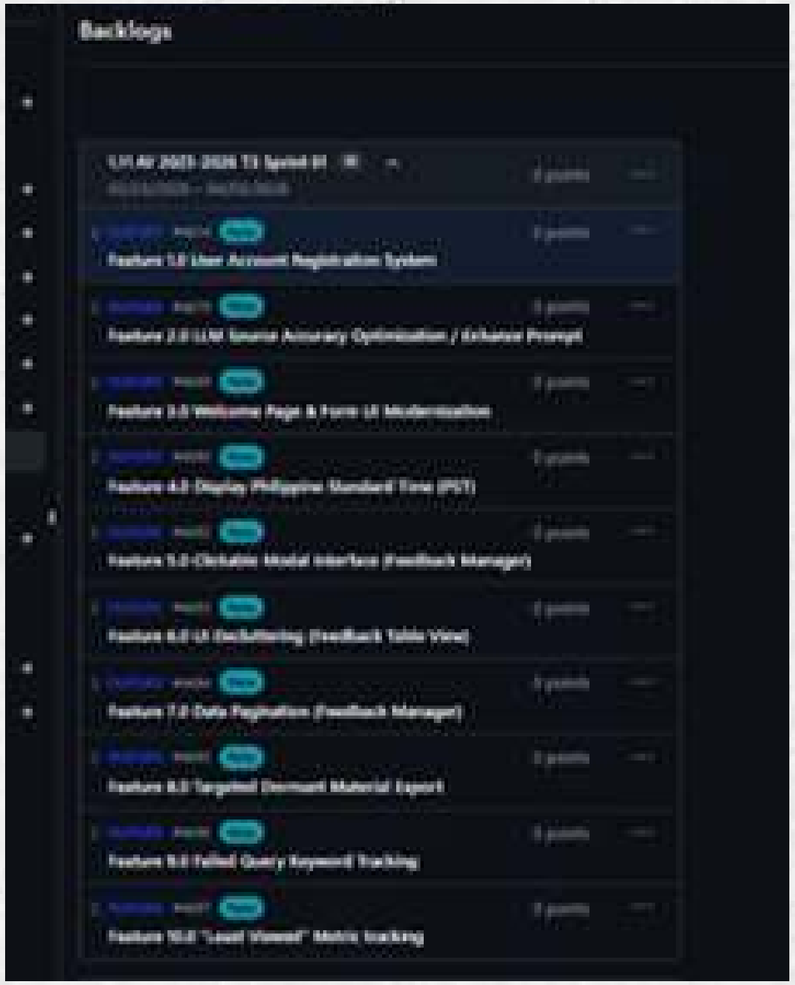

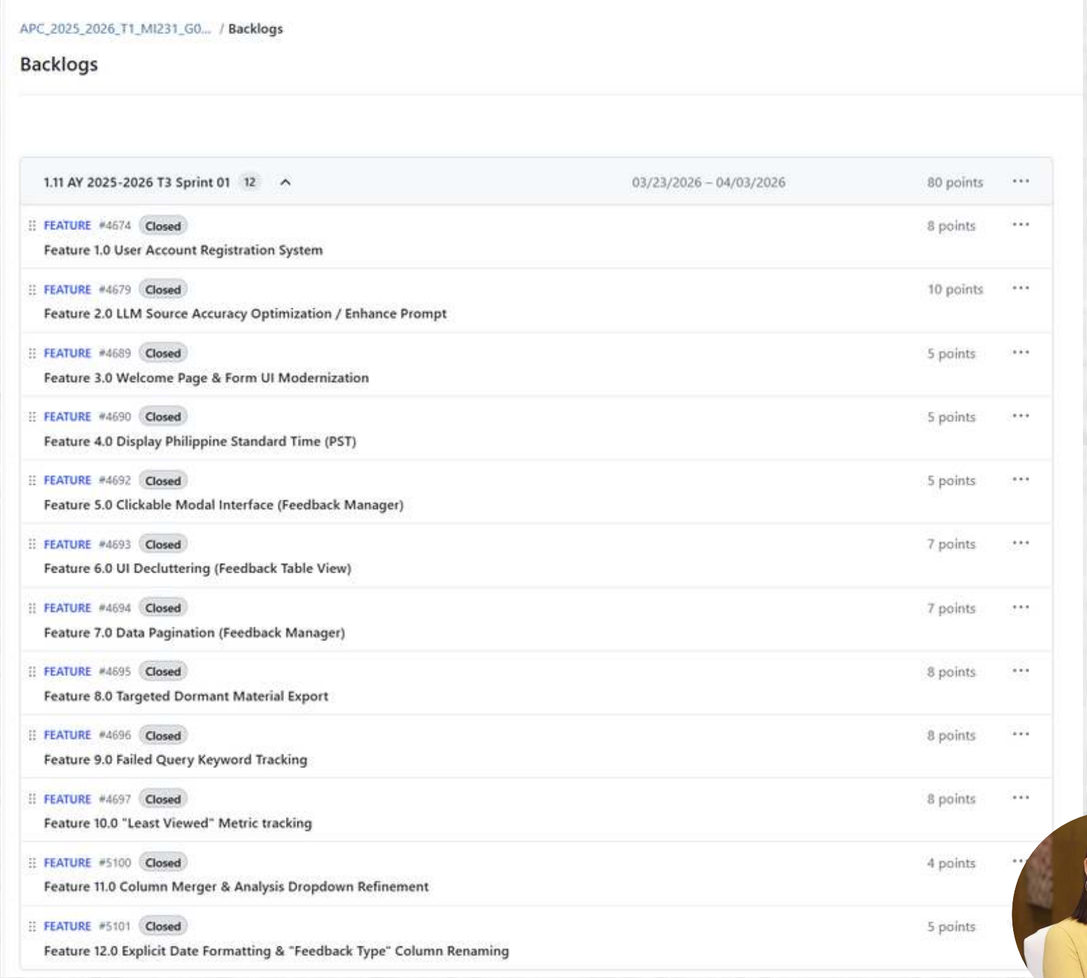

Tomon, Tracie

DOST ScINET-PHIL
http://scinet.dost.gov.ph

Agile Scrum Ceremonies

Sprint Review

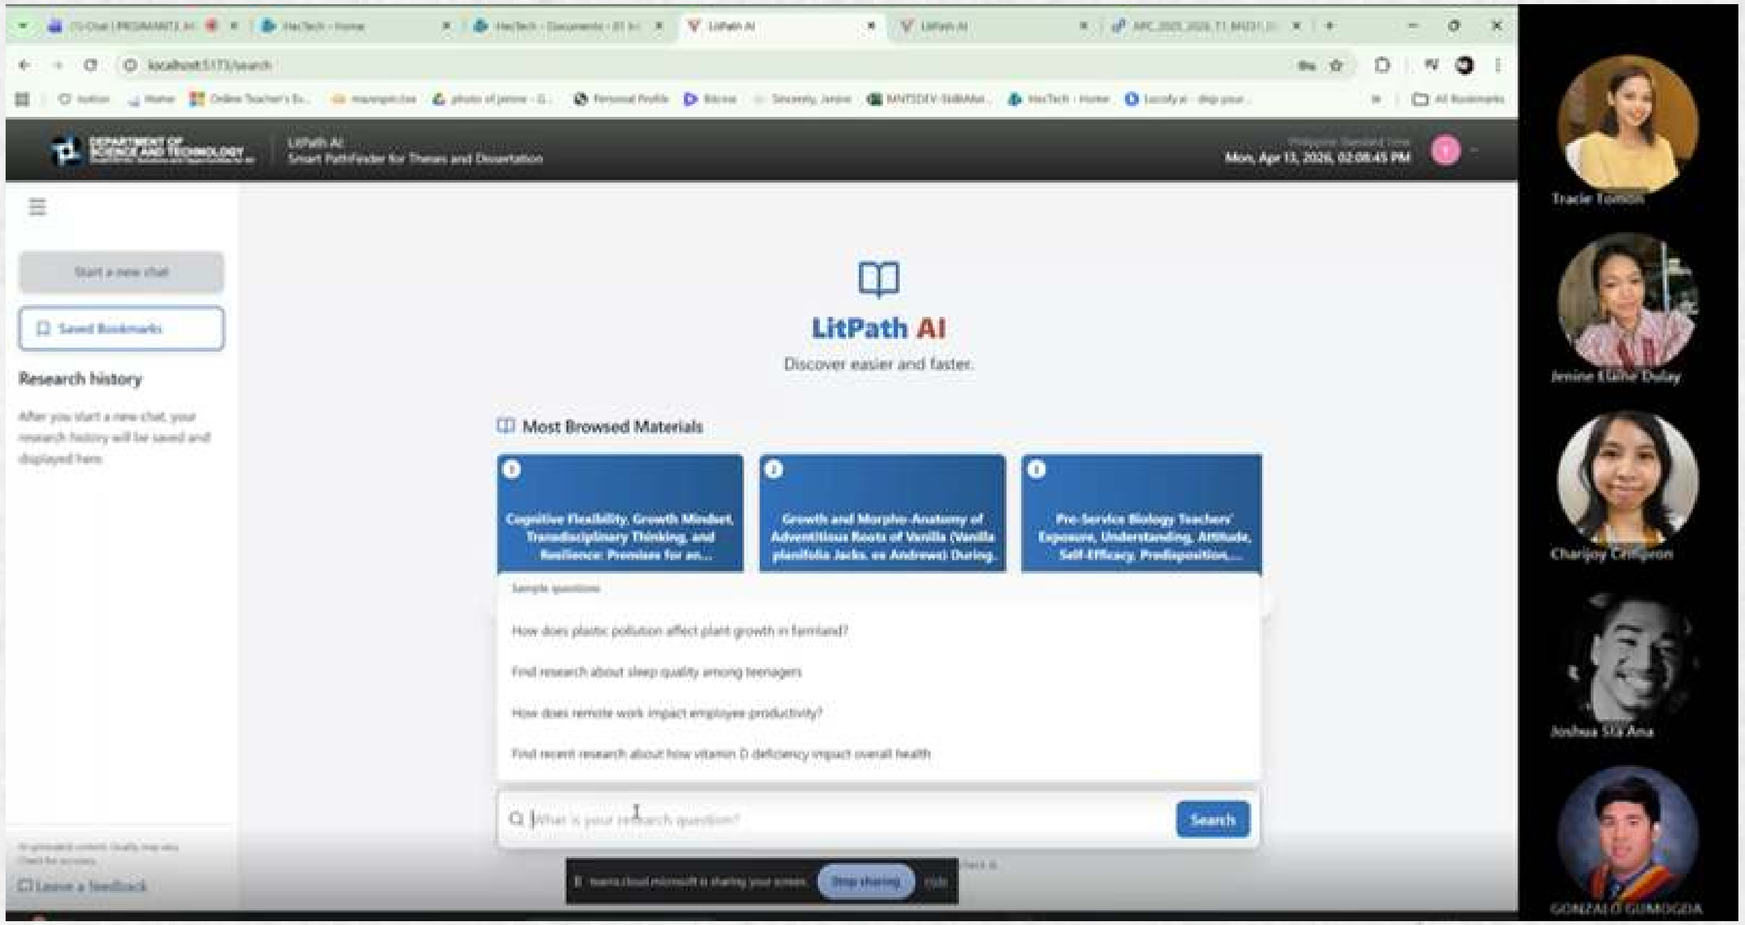

Sta Ana, Joshua

AGILE SCRUM DOCUMENTS

DOST ScINET-PHIL
http://scinet.dost.gov.ph

Agile Team Charter

Tools

Communication

Development

Project Tracking

Document Management

Dulay, Jenine Elaine

DOST ScINET-PHIL
http://scinet.dost.gov.ph

Agile Team Charter

Rules of Behavior

Communication
(Attendance, Feedback)

Task Management (Task
Tracking, Documentation)



Project Control (Escalation,
Change Control)

Quality Assurance (Review)

Dulay, Jenine Elaine

Agile Scrum Documents

Agile Team Values

Team Foundation

Motivation: Graduate successfully, gain real experience, develop skills, deliver reliable solutions

Leadership: Trust assigned leader to guide direction and keep team on track

Communication: "Tap system" for accountability, share availability, regular updates

Team Building: Regular meetings, in-person collaboration, food trips, performance check-ins

Team Beliefs

- ✓ Learning starts with action
- ✓ Mistakes are part of growth
- ✓ Good communication prevents problems
- ✓ Supporting each other improves outcomes
- ✓ Respect time, ideas, and differences

Our 6 Core Values

1. **Initiative** - Act independently using skills and judgment
2. **Commitment** - Give best effort for high-quality results
3. **Transparency** - Be honest about capabilities and limitations
4. **Flexibility** - Adapt to changes and support team goals
5. **Effective Communication** - Share clearly and listen actively
6. **Accountability** - Own responsibilities and outcomes

Team Traditions

- Progress updates & hindrance sharing
- Peer support when stuck
- Weekly meetings: wins, improvements, tasks
- Meeting notes for everyone
- Goal-setting before tasks
- Celebrate milestones with gratitude

Sta Ana, Joshua

PMBOK INITIATION PHASE

PROJECT CHARTER

Project Scope and Business Need

Project Scope

- Develop standalone AI-powered web app for DOST-STII Library
- Enables semantic search for theses and dissertations
- Includes features: summaries, citations, bookmarks, history, admin dashboard
- Covers design, development, testing, and deployment

Business Need

- Current OPAC has limited keyword search and vague results
- Need for faster, more relevant research outputs
- Improve efficiency for students and library staff
- Leverage AI (embeddings & LLMs) for better search experience

Dulay, Jenine Elaine

DOST ScINET-PHIL
http://scinet.dost.gov.ph

PROJECT CHARTER

Objectives

Improve accuracy and relevance of search results

Enhance research efficiency for students and staff



Provide faster query processing and result display



Enable intelligent features (Citations,bookmark, follow-up queries)

Dulay, Jenine Elaine

DOST ScINET-PHIL
http://scinet.dost.gov.ph

PROJECT CHARTER

Milestone Schedule

Milestone	Target Date	Status
Project Scoping	April 2025	Completed
Information Gathering	April 2025	Completed
Completion of Project Deliverables & Documentation	June 2025	Completed
Design Thinking Process (Stages 1–5)	Aug 2025	Completed
Core UI Development (System UI, Citation Generator, Bookmark)	Sep – Oct 2025	Completed
AI Search Engine, Generate Overview, Feedback Mechanism & Admin Dashboard	Oct 2025 – Jan 2026	Completed
Feature Refinement & Client Feedback Integration	Feb – Mar 2026	Completed
Continued Development & Performance Optimization (incl. codebase restructuring)	Mar – Apr 2026	In Progress
Proxmox Server Deployment & Internal Testing	Apr 2026	In Progress
Bug Fixes & Usability Testing	May – Jun 2026	Not Started
Final Deployment	Jun – Jul 2026	Not Started

Tomon, Tracie

DOST ScINET-PHIL
http://scinet.dost.gov.ph

PROJECT BRIEF

🔍 The Challenge

- OPAC relies on exact-match keywords → missed relevant studies
- <70% search relevance; ~15 mins wasted per session filtering results
- Search queries take >60 seconds (vs. 30-sec industry standard)
- No AI, no auto-citations, no bookmarking → manual, error-prone workflow

🎯 Project Objectives

✅ Boost search precision → Target: ≥3.5/5 user satisfaction
✅ AI semantic search → ≥70% relevance in top 10 results
✅ Faster UX → Sub-30-sec response time
✅ One-click citations → APA 7, MLA 9, Chicago, IEEE support

👥 Target Users

🎓 Students & Researchers — faster, smarter literature discovery
⚙️ DOST-STII Admins — reference support + usage insights

Project Timeline: Mar 2025 – Jun/Jul 2026 | PM: Tracie Tomon

✨ Core Features (Scope)

- Standalone AI-powered web app (independent of OPAC)
- Semantic search engine: understands research *intent*, not just keywords
- Auto citation generator + bookmarking + feedback tools
- Admin analytics dashboard: track trends & usage

📦 Key Deliverables

🚀 Production-ready prototype (fully tested & deployable via Proxmox)
📚 Complete documentation: technical manual, user guide, final report

📊 Success Criteria

✔️ 100% feature-complete, bug-free application
✔️ ≥3.5/5 avg. user satisfaction (students & DOST staff)
✔️ Faster search performance vs. legacy OPAC
✔️ Formal stakeholder sign-off on all deliverables

Sta Ana, Joshua

Business Case

Business Case Analysis Team

Project Adviser

Client



Project Manager

Development Team

Cempron, Charijoy

Business Case

Strategic Alignment

Plan	Goals/Objectives	Relationship to Project
DOST-STII Digital Information Access Plan	Improve accessibility and discoverability of academic resources	Enhances thesis and dissertation discoverability through AI-powered semantic search
DOST-STII Technology Modernization Plan	Modernize service delivery through technology	Introduces AI-powered search, citation generation, and analytics
DOST-STII Research Support and Scholar Empowerment Plan	Support students/researchers in conducting efficient and well-documented research	Cuts response time to under 5 minutes and offers tools for organizing and citing materials

Cempron, Charijoy

Business Case

Cost Benefit Analysis

Action	Action Type	Description
System Development by HecTech	Cost	4-member HecTech team contributing labor across six development phases
Cloud Hosting & Infrastructure	Cost	Hosted on Proxmox server for development
AI / LLM API Integration (Gemini AI)	Cost	Operational costs for RAG and Gemini AI during development and live operation
Reduction in manual research time	Benefit	Semantic search reduces search time from 15 minutes to a few minutes per session
Elimination of manual citation formatting	Benefit	Automated citation generation in APA, MLA, Chicago, and IEEE removes manual formatting
Improved system response time	Benefit	Query response time reduced from 10 minutes to under 5 minutes

Cempron, Charijoy

PMBOK PLANNING PHASE

DOST ScINET-PHIL
http://scinet.dost.gov.ph

Stakeholder Analysis

Name	Department / Company	Position	Objectives, Requirements, Interests	Project Contribution	Resistance	Power and Interest
Mr. Napoleon Juanillo, Jr. PhD	DOST-STII	Assistant Secretary for Technology Transfer, Communications and Commercialization and Officer-in-Charge, Office of the Director	Research commercialization and partnership development	Provides projects to be worked on by the students	Concerned about budget allocations	High
Ms. Khasian Romulo	DOST-STII	Science Research Specialist II	Efficient research discovery and modernize search capabilities	Requirements definition, supports work, and approves deliverables	Concerned about changing initial requirements mid-project	High
Mr. Jonathan Abalon	DOST-STII	Science Research Specialist II	Improve user satisfaction and increase research utilization	System access and technical support	Concerned about the problems that might arise during system integration	High
Mr. Sean Sanchez	APC	Project Based Learning Coordinator	Educational innovation and and partnership development	Project sourcing	Concerned about partner organizations modifying project scope	High
Mr. Gonzalo Guumogda	APC	SoCIT Faculty/ Project Adviser	Student academic success and skill development	Project guidance, technical mentorship and approves deliverables	Concerned about timeline delays of the deliverables	High
Mr. Jose Quesada	APC	SOCIT Professor	Student academic success and learning outcomes	Technical mentorship and academic evaluation	Concerned about insufficient time for mentorship due to	Medium
End Users	N/A	End Users	Faster research discovery and friendly search interface	User feedback and system testing	Concerned about the interface change of the system	Medium
HecTech Team	APC	Project Developers	Academic achievement and successful project delivery	System development and client communication	Concerned about technical challenges and time constraints	High

Cempron, Charijoy

DOST ScINET-PHIL
http://scinet.dost.gov.ph

PMBOK: Initiation phase

Stakeholder Management Strategy

🎯 Strategy Purpose

- Ensure all stakeholders are identified, understood & engaged
- Gain support • Reduce resistance • Balance competing interests
- Enable proactive communication & early conflict resolution

📊 Engagement Strategy (Power/Interest Matrix)

🔴 **Manage Closely** (High Power, High Interest)
→ Romulo & Abalon: Weekly updates • Co-design sessions • Priority feedback loops

🟡 **Keep Satisfied** (High Power, Mid Interest)
→ Asst. Sec. Juanillo: Milestone reports • Executive summaries • Formal sign-offs

🟢 **Keep Informed** (Low Power, High Interest)
→ Faculty, Developers, End Users: Bi-weekly digests • Demo sessions • Feedback channels

⚪ **Monitor** (Low Power, Low Interest)
→ External observers: Quarterly highlights • Public project updates

🔄 Communication & Validation Process

1️⃣ Internal brainstorming (APC team) → 2️⃣ Adviser validation → 3️⃣ DOST-STII alignment → 4️⃣ Iterative updates

📌 *Stakeholder register reviewed monthly • New stakeholders added as needed • Concerns logged & addressed proactively*

Stakeholder	Role	Power	Interest
🏛️ Asst. Sec. Napoleon K. Juanillo Jr., PhD	Budget/Approval Authority	⭐⭐⭐⭐⭐	⭐⭐⭐
👩‍💼 Khasian Eunice Romulo (Primary POC)	Requirements & Deliverables	⭐⭐⭐⭐	⭐⭐⭐⭐⭐
👨‍💼 Jonathan Abalon (Alternate POC)	Technical Liaison	⭐⭐⭐⭐	⭐⭐⭐⭐⭐
🎓 Manuel Sebastian S. Sanchez (PBL Coordinator)	Partnership Management	⭐⭐⭐	⭐⭐⭐⭐
👩‍🏫 SoCIT Faculty Advisers	Technical Mentorship	⭐⭐⭐	⭐⭐⭐⭐⭐
💻 Student Developers	System Development	⭐⭐	⭐⭐⭐⭐⭐
🎓 End Users (Students/ Researchers)	System Beneficiaries	⭐	⭐⭐⭐⭐

Tomon, Tracie

DOST ScINET-PHIL
http://scinet.dost.gov.ph

PMBOK: Initiation phase

Statement of Work

🎯 Project Purpose

Develop a **standalone AI-powered web application** to enhance discovery of DOST-STII Library's thesis/dissertation collection—solving OPAC's exact-match search limits, slow performance, and lack of research support tools.

✅ In-Scope Deliverables

- **AI Semantic Search Engine** – RAG + Gemini AI for intent-based queries & result re-ranking
- **Standalone Web App** – Independent UI, separate from existing OPAC
- **Client-Provided Database** – Sample theses/dissertations from DOST-STII only
- **Auto Citation Generator** – APA 7, MLA 9, Chicago, IEEE formats
- **Research Tools** – Bookmarking + user feedback mechanism
- **Admin Analytics Dashboard** – Search trends, usage patterns, interaction insights

❌ Out-of-Scope

🚫 Full-text digitization of non-digitized materials
🚫 Direct management/alteration of library's primary collection records

🔐 Key Constraints & Requirements

- **Database**: Independent repo using client-provided sample papers only
- **Privacy**: Compliant with Data Privacy Act of 2012 (RA 10173)
- **Security**: HTTPS/SSL encryption for all connections
- **Team**: 4-member APC-HecTech student team (no outsourcing)
- **Capacity**: Part-time execution (~10 hrs/week per member)

📅 Key Milestones

Phase	Target Date	Status
🚀 Project Scoping & Design Thinking	Apr–Aug 2025	✅ Done
💻 Core UI + AI Engine Development	Sep 2025–Jan 2026	✅ Done
🔄 Refinement + Client Feedback	Feb–Mar 2026	✅ Done
⚙️ Optimization + Proxmox Testing	Apr 2026	🟡 In Progress
🐞 Bug Fixes + Usability Testing	May–Jun 2026	⚪ Pending
🎯 Final Deployment & Handover	Jun–Jul 2026	⚪ Pending

✔️ Acceptance Criteria (Sponsor Sign-Off)

✅ 100% functional standalone app with all features operational
✅ ≥70% relevance accuracy in top 10 search results
✅ ≥3.5/5 average user satisfaction (students & DOST staff)
✅ Formal approval by Project Sponsors: *Khasian Romulo & Jonathan Abalon*

Sta Ana, Joshua

DOST ScINET-PHIL
http://scinet.dost.gov.ph

PMBOK: Planning Phase

Communications Management Plan

Communication Type	Medium	Frequency	Audience	Deliverable	Format
Sprint Planning	Face to face or Microsoft Teams	Once per sprint	Project Team	Sprint Plan, MOTM	Video recording stored on Microsoft Teams channel and SharePoint
Daily Stand-up	Face to face or Microsoft Teams	Daily during active sprints	Project Team	Stand-up MOTM	Video recording stored on Microsoft Teams channel, verbal updates
Backlog Refinement	Face to face or Microsoft Teams	Once per sprint	Project Team	Updated Product Backlog	Video recording stored on Microsoft Teams channel and OpenProject
Sprint Review	Face to face or Microsoft Teams	Once per sprint	Project Team, Project Adviser, Client	Sprint Demo, MOTM	Video recording stored on Microsoft Teams channel and SharePoint

Dulay, Jenine Elaine

DOST ScINET-PHIL
http://scinet.dost.gov.ph

PMBOK: Planning Phase

Communications Management Plan

Sprint Retrospective	Face to face or Microsoft Teams	Once per sprint	Project Team	Project Manager	Retrospective MOTM	Video recording stored on Microsoft Teams channel. SharePoint, ans Trello Board
Project Status Report	Face to face or Microsoft Teams	Per sprint	Project Sponsor, Project Adviser	Project Manager	Project Status Report	Soft copy sent via Viber
Client Coordination Meeting	Face to face or Microsoft Teams or Viber	As needed	Project Manager, Client	Project Manager	MOTM	Soft copy archived on SharePoint

Dulay, Jenine Elaine

PMBOK: Planning Phase

Scope Management Plan

Collect Requirements	Gather and document requirements through stakeholder interviews, Design Thinking activities, and the Project Charter.
Define Scope	Establish project boundaries, deliverables, constraints, and features based on OPAC limitations and client needs.
Create WBS	Break down project work into manageable packages organized by phases and tracked in OpenProject.
Verify Scope	Review and validate deliverables with the Project Manager and Khasian Eunice Romulo through milestone approvals.
Control Scope	Manage scope changes through formal change requests, impact assessment, and sponsor approval to prevent scope creep.

Dulay, Jenine Elaine

PMBOK: Planning Phase

Work Breakdown Structure

OpenProject Link

Dulay, Jenine Elaine

DOST ScINET-PHIL
http://scinet.dost.gov.ph

PMBOK: Planning Phase

Schedule Management Plan

🎯 Schedule Approach

- **Tool**: OpenProject for Gantt charts, task tracking & milestone management
- **Method**: WBS-driven → Activity sequencing → Duration estimating → Resource assignment
- **Workflow**: Bi-weekly reviews • Sprint-based development • Academic-aligned pacing

⏱️ Team Capacity (Part-Time Students)

Timeframe	Availability	Assigned Value
📅 Weekly	Evening sessions (4–6 hrs) + occasional weekends	**10 hrs/member**
📆 Monthly	Standard 4-week academic month	**40 hrs/member**
💰 Costing	Flat rate for budgeting in OpenProject	**₱500/hr**

🚀 Key Milestones & Status

Milestone	Target Date	Status
📋 Project Scoping & Design Thinking	Apr–Aug 2025	✅ Completed
💻 Core UI + AI Engine Development	Sep 2025–Jan 2026	✅ Completed
🔄 Refinement + Client Feedback	Feb–Mar 2026	✅ Completed
⚙️ Optimization + Proxmox Testing	Mar–Apr 2026	🟡 In Progress
🐞 Bug Fixes + Usability Testing	May–Jun 2026	⚪ Pending
🎯 Final Deployment & Handover	Jun–Jul 2026	⚪ Pending

👥 Roles in Schedule Management

- **Tracie (PM)**: Schedule creation, OpenProject maintenance, sponsor alignment
- **Jenine & Charijoy (Devs)**: Task estimation, development execution, progress reporting
- **Joshua (QA)**: Testing timelines, bug tracking, QA milestone validation
- **Khasian Romulo (Sponsor)**: Schedule approval • Change request sign-off (>10% variance)

👥 Roles in Schedule Management

- **Tracie (PM)**: Schedule creation, OpenProject maintenance, sponsor alignment
- **Jenine & Charijoy (Devs)**: Task estimation, development execution, progress reporting
- **Joshua (QA)**: Testing timelines, bug tracking, QA milestone validation
- **Khasian Romulo (Sponsor)**: Schedule approval • Change request sign-off (>10% variance)

🔁 Schedule Control & Changes

📊 **Monitoring**: Bi-weekly Teams reviews • OpenProject updates • Blocker logging
📬 **Channels**: Teams (internal) • Viber (client) • OpenProject (official tracker)

⚠️ **Change Threshold**: Formal approval required if:
→ Single task variance ≥10% • OR • Overall timeline shift ≥10%

🔄 **Re-baselining**: Triggered by approved scope changes impacting timeline (e.g., new AI features, deployment adjustments)

Tomon, Tracie

DOST ScINET-PHIL
http://scinet.dost.gov.ph

PMBOK: Planning Phase

Quality Management Plan: Quality Assurance

📋 Quality Purpose

Ensure a **secure, accurate, high-performing** AI-powered research tool that meets DOST-STII standards, Philippine Data Privacy Act (RA 10173), and user expectations.

⚖️ Dual-Focus Approach

Product Quality 🧩	Process Quality ⚙️
• AI relevance ≥70% top-10 results • API response <2s standard / <5s streaming • System uptime ≥99.5% • UX satisfaction ≥3.5/5	• 100% peer-reviewed PRs • CI/CD success rate ≥95% • SDS documentation compliance • Sprint delivery adherence

📊 Key Quality Metrics

- **Performance**: Search latency <30s • Vector similarity threshold <1.5
- **Accuracy**: Citation generator verified for APA/MLA/Chicago/IEEE
- **Security**: OWASP Top 10 compliance • PBKDF2 hashing • HTTPS/SSL
- **Testing**: ≥80% unit/integration test coverage • Zero critical bugs at launch
- **Privacy**: DPA 2012 compliance for admin accounts • Anonymous public search

🔍 QA vs QC Activities

Quality Assurance (Process)	Quality Control (Product)
✅ Weekly code reviews & merge checks	✅ Functional & UAT testing
✅ CI/CD pipeline audits	✅ AI response validation (citation-backed answers)
✅ AI pipeline benchmarking (≥85% relevance)	✅ Security penetration testing
✅ Documentation compliance checks	✅ Performance/load testing pre-launch

📝 Quality Logs & Tracking

📋 **QA Log**: Tracks process metrics (code review rate, CI/CD success, AI accuracy)

🐞 **QC Log**: Records product defects, test results, and resolution status

🔄 **Review Cycle**: Bi-weekly sprint reviews • Monthly security audits • Pre-release UAT sign-off

Sta Ana, Joshua

DOST ScINET-PHIL
http://scinet.dost.gov.ph

Human Resource Plan

Resource Calendar

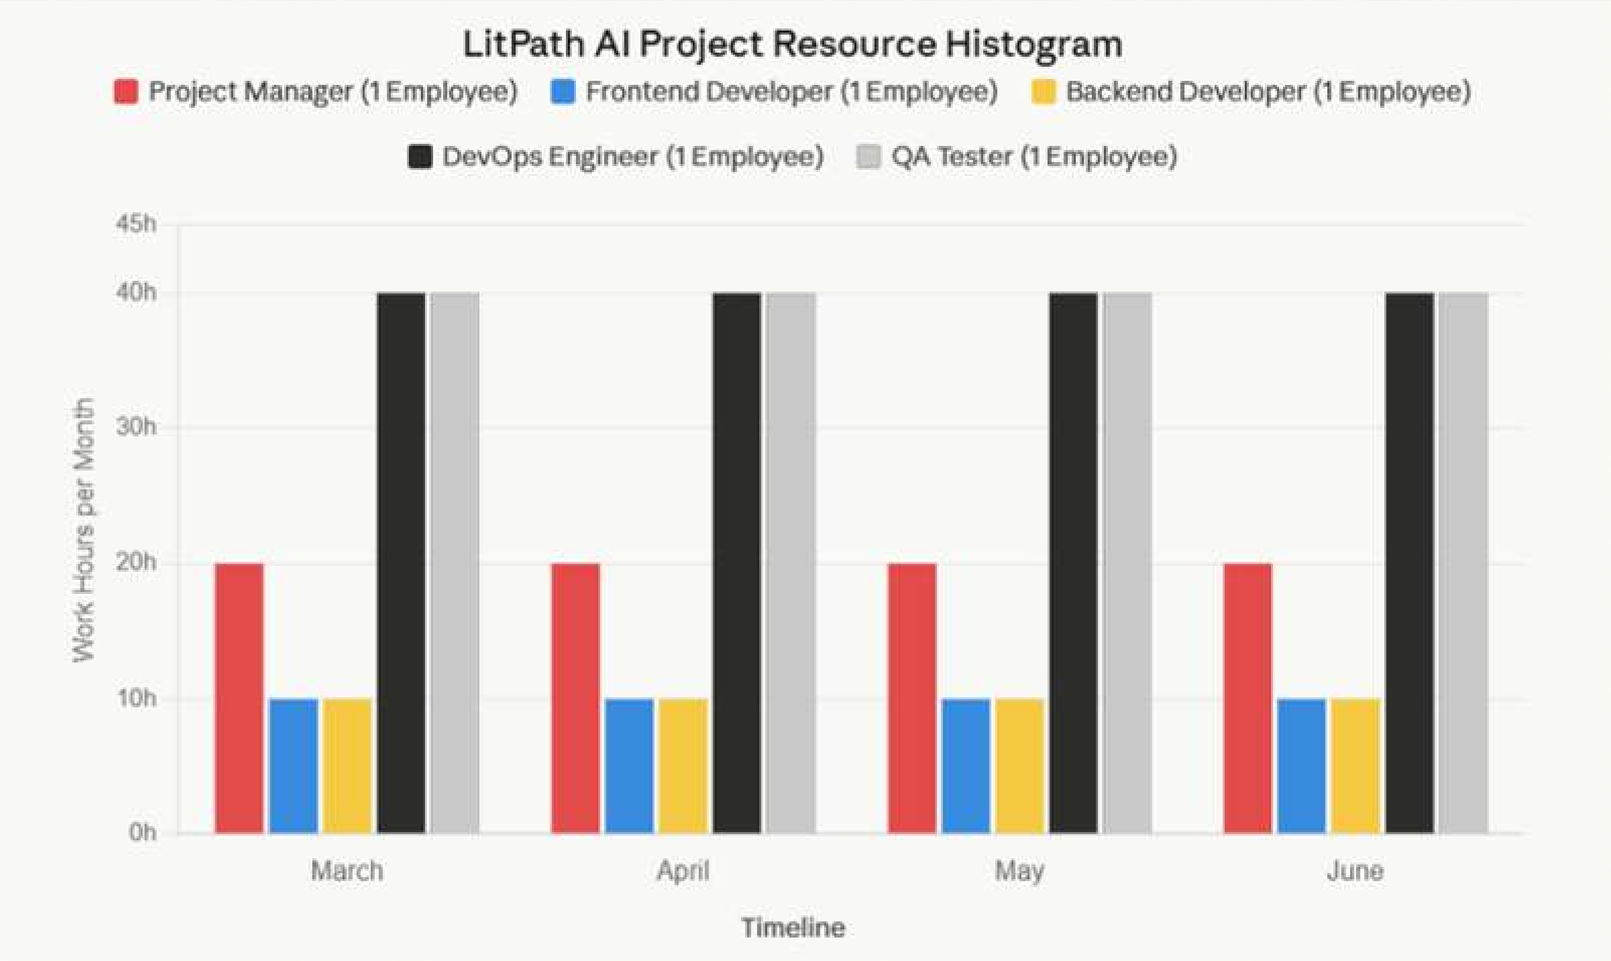

Cempron, Charijoy

COSTS

SYSTEM DESIGN DOCUMENT

DOST ScINET-PHIL
http://scinet.dost.gov.ph

System Design Document

Hardware & Software Detailed Design

React
Frontend

django
Backend

supabase
Database

Gemini
AI Processing

ChromaDB
Semantic Search

Proxmox
Deployment

Hardware: i5 CPU, 32GB RAM, SSD + HDD Storage

Cempron, Charijoy

OPENPROJECT

Tomon, Tracie

DOST ScINET-PHIL
http://scinet.dost.gov.ph

OPENPROJECT

RACI

Responsible*	TT Tracie Tomon
Accountable	TT Tracie Tomon
Consulted	GG Gonzalo Gumogda
Informed	K@ khasian.romulo @stii.dost.gov.ph

Responsible*	JD Jenine Elaine Dulay
Accountable	TT Tracie Tomon
Consulted	GG Gonzalo Gumogda
Informed	K@ khasian.romulo @stii.dost.gov.ph J@ jonathan.abalon @stii.dost.gov.ph

Responsible*	JA Joshua Sta Ana
Accountable	TT Tracie Tomon
Consulted	GG Gonzalo Gumogda
Informed	J@ jonathan.abalon @stii.dost.gov.ph K@ khasian.romulo @stii.dost.gov.ph

Responsible*	CC Charijoy Cempron
Accountable	TT Tracie Tomon
Consulted	GG Gonzalo Gumogda
Informed	K@ khasian.romulo @stii.dost.gov.ph

Tomon, Tracie
